# TD Centre Redevelopment

## 3 Week Look-Ahead Schedule

Issued: Fri 2/15/13

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 1 | Form & pour concrete footings at Gridline 5 | 7 days | Thu 2/07/13 | Fri 2/15/13 | |
| 2 | Form & pour concrete shear wall at Gridline A (1st Level) | 4 days | Wed 2/13/13 | Mon 2/18/13 | |
| 3 | Form & pour concrete shear wall at Gridline A (2nd Level) | 4 days | Mon 2/18/13 | Thu 2/21/13 | |
| 4 | Place reinforcing steel in footings along Gridline A and Gridline 5 | 2 days | Wed 2/13/13 | Thu 2/14/13 | |
| 5 | NEW emergency exit to George Street | 10 days | Mon 2/04/13 | Fri 2/15/13 | |
| 6 | NIGHT SHIFT - Clean existing wall & install reinforcing dowels at Gridline 5 | 15 days | Wed 2/13/13 | Tue 3/05/13 | |
| 7 | Remove walls at garbage room | 2 days | Thu 2/14/13 | Fri 2/15/13 | |
| 8 | Interior excavation to underside of existing footings | 10 days | Fri 2/15/13 | Thu 2/28/13 | |
| 9 | Install underground pluming in new office tower | 3 days | Wed 2/13/13 | Fri 2/15/13 | |
| 10 | Backfill underground plumbing | 1 day | Mon 2/18/13 | Mon 2/18/13 | 9 |
| 11 | Prepare for slab on grade concrete pour (1st pour) | 4 days | Thu 2/14/13 | Tue 2/19/13 | |
| 12 | Install wire mesh & reinforcing steel for slab on grade | 2 days | Wed 2/20/13 | Thu 2/21/13 | 11 |
| 13 | Pour concrete for slab on grade (1st pour) | 1 day | Fri 2/22/13 | Fri 2/22/13 | 12 |

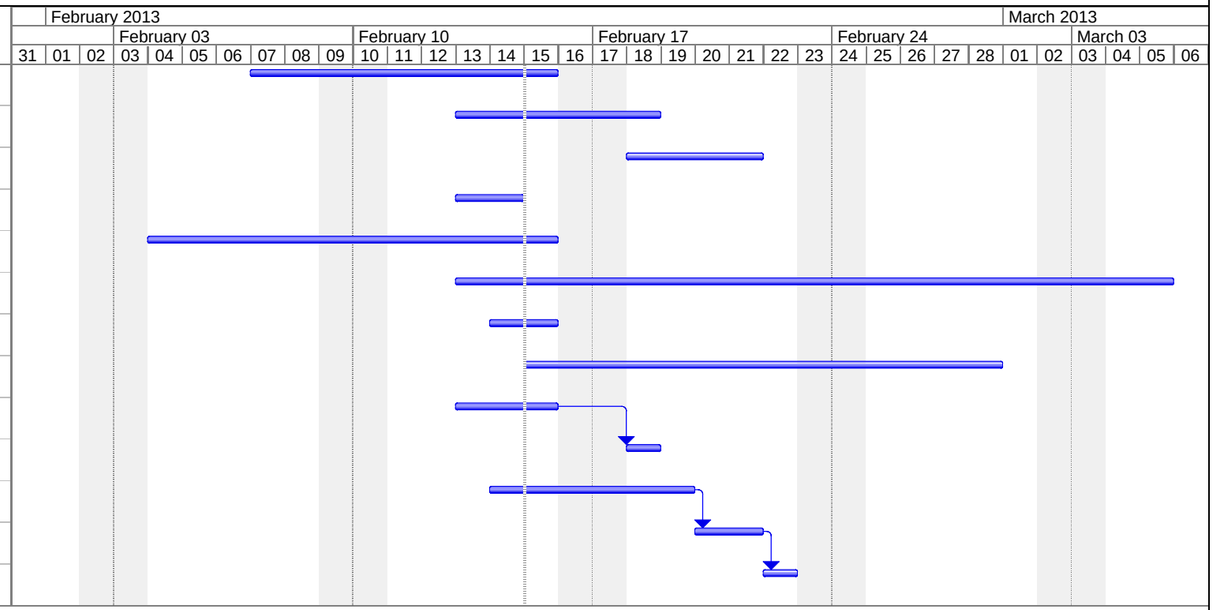


EllisDon
We build on great relationships™

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
